


Activity Name	Original Duration	Start	Finish	2020		2021								
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
<b>Papa John's</b>	150	12-Nov-20 A	01-Jul-21											
<b>Project Milestones</b>	150	12-Nov-20 A	01-Jul-21	<ul style="list-style-type: none"> <li>◆ GC RFP Issued</li> <li>◆ GC RFP Questions Due</li> <li>◆ GC RFP Questions Answered</li> <li>◆ GC RFP Due</li> <li>■ GC Virtual Interviews</li> <li>◆ GC Selection</li> <li>◆ Substantial Completion</li> </ul>										
GC RFP Issued	0	12-Nov-20 A												
GC RFP Questions Due	0		23-Nov-20 A											
GC RFP Questions Answered	0		25-Nov-20 A											
GC RFP Due	0		04-Dec-20											
GC Virtual Interviews	4	09-Dec-20	14-Dec-20											
GC Selection	0		16-Dec-20											
Substantial Completion	0		01-Jul-21											
<b>Design</b>	93	01-Dec-20 A	13-Apr-21	<ul style="list-style-type: none"> <li>■ Workplace Schematic Design</li> <li>■ Test Kitchen Schematic Design</li> <li>■ Workplace Schematic Design Budget Due</li> <li>■ Workplace Design Development</li> <li>■ Test Kitchen Design Development</li> <li>■ Test Kitchen Schematic Design Budget Pricing Due</li> <li>◆ Workplace Design Development Presentation</li> <li>◆ Workplace DD Doc Client Approval</li> <li>■ Workplace Construction Documents</li> <li>■ Workplace Design Development Budget Pricing Due</li> <li>■ Test Kitchen Design Development Pricing Due</li> <li>◆ Test Kitchen Design Development Presentation</li> <li>◆ Workplace CD Page Turn &amp; Final Comments</li> <li>■ Workplace Final Construction Docs Issued</li> <li>◆ Test Kitchen DD Doc Client Approval</li> <li>■ Test Kitchen Construction Documents</li> <li>■ Test Kitchen Final Pricing Due</li> </ul>										
Workplace Schematic Design	22	01-Dec-20 A	30-Dec-20											
Test Kitchen Schematic Design	20	15-Dec-20	11-Jan-21											
Workplace Schematic Design Budget Due	10	31-Dec-20	13-Jan-21											
Workplace Design Development	21	05-Jan-21	02-Feb-21											
Test Kitchen Design Development	36	12-Jan-21	02-Mar-21											
Test Kitchen Schematic Design Budget Pricing Due	16	13-Jan-21	03-Feb-21											
Workplace Design Development Presentation	0		03-Feb-21											
Workplace DD Doc Client Approval	0		04-Feb-21											
Workplace Construction Documents	20	05-Feb-21	04-Mar-21											
Workplace Design Development Budget Pricing Due	9	05-Feb-21	17-Feb-21											
Test Kitchen Design Development Pricing Due	5	03-Mar-21	09-Mar-21											
Test Kitchen Design Development Presentation	0		03-Mar-21											
Workplace CD Page Turn & Final Comments	0		05-Mar-21											
Workplace Final Construction Docs Issued	5	08-Mar-21	12-Mar-21											
Test Kitchen DD Doc Client Approval	0		09-Mar-21											
Test Kitchen Construction Documents	10	10-Mar-21	23-Mar-21											
Test Kitchen Final Pricing Due	15	24-Mar-21	13-Apr-21											
<b>Procurement</b>	90	18-Feb-21	23-Jun-21	<ul style="list-style-type: none"> <li>■ Award and Release Mechanical Scope</li> <li>■ Award and Release Electrical Scope</li> <li>■ Award and Release Plumbing Scope</li> <li>■ Award and Release Fire Protection Scope</li> <li>■ Award and Release Structural Steel Scope</li> <li>■ Award and Release Floorcovering Scope</li> <li>■ Award and Release Doors, Frames &amp; Hardware Sc</li> <li>■ Award and Release Glass &amp; Glazing Scope</li> </ul>										
<b>Award</b>	16	18-Feb-21	11-Mar-21											
Award and Release Mechanical Scope	5	18-Feb-21	24-Feb-21											
Award and Release Electrical Scope	5	18-Feb-21	24-Feb-21											
Award and Release Plumbing Scope	5	18-Feb-21	24-Feb-21											
Award and Release Fire Protection Scope	5	18-Feb-21	24-Feb-21											
Award and Release Structural Steel Scope	5	18-Feb-21	24-Feb-21											
Award and Release Floorcovering Scope	5	18-Feb-21	24-Feb-21											
Award and Release Doors, Frames & Hardware Sc	5	18-Feb-21	24-Feb-21											
Award and Release Glass & Glazing Scope	5	18-Feb-21	24-Feb-21											

Activity Name	Original Duration	Start	Finish	2020		2021											
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep			
Award and Release Millwork Scope	5	18-Feb-21	24-Feb-21						█								
Early Award and Release Kitchen Equipment Scop	2	10-Mar-21	11-Mar-21						█								
<b>Submittals</b>	<b>85</b>	<b>25-Feb-21</b>	<b>23-Jun-21</b>						█								
Mechanical - Prepare and Submit Shop Drawings & S	10	25-Feb-21	10-Mar-21						█								
Electrical - Prepare and Submit Shop Drawings & S	10	25-Feb-21	10-Mar-21						█								
Plumbing - Prepare and Submit Shop Drawings & S	5	25-Feb-21	03-Mar-21						█								
Fire Protection - Prepare and Submit Shop Drawing	20	25-Feb-21	24-Mar-21						█								
Structural Steel - Prepare and Submit Shop Drawin	20	25-Feb-21	24-Mar-21						█								
Floorcovering - Prepare and Submit Submittals / Sa	5	25-Feb-21	03-Mar-21						█								
Doors, Frames & Hardware - Prepare and Submit S	10	25-Feb-21	10-Mar-21						█								
Interior Glass & Glazing - Prepare and Submit Shop	20	25-Feb-21	24-Mar-21						█								
Millwork - Prepare and Submit Shop Drawings & Su	20	25-Feb-21	24-Mar-21						█								
GC Review & Submit Plumbing Submittals	5	04-Mar-21	10-Mar-21						█								
GC Review & Submit Floorcovng Submittals	5	04-Mar-21	10-Mar-21						█								
GC Review & Submit Mechanical Submittals	5	11-Mar-21	17-Mar-21						█								
GC Review & Submit Electrical Submittals	5	11-Mar-21	17-Mar-21						█								
Design Review & Approve Plumbing Submittals	10	11-Mar-21	24-Mar-21						█								
Design Review & Approve Floorcovering Submittals	10	11-Mar-21	24-Mar-21						█								
GC Review & Submit Doors, Frames & Hardware S	5	11-Mar-21	17-Mar-21						█								
Kitchen Equipment - Prepare and Submit Shop Dr	15	12-Mar-21	01-Apr-21						█								
Design Review & Approve Mechanical Submittals	10	18-Mar-21	31-Mar-21						█								
Design Review & Approve Electrical Submittals	10	18-Mar-21	31-Mar-21						█								
Design Review & Approve Doors, Frames & Hardw	10	18-Mar-21	31-Mar-21						█								
GC Review & Submit Fire Protection Submittals	5	25-Mar-21	31-Mar-21						█								
GC Review & Submit Structural Steel Submittals	5	25-Mar-21	31-Mar-21						█								
GC Review & Submit Interior Glass & Glazing Subn	5	25-Mar-21	31-Mar-21						█								
GC Review & Submit Millwork Submittals	5	25-Mar-21	31-Mar-21						█								
Plumbing - Release & Procure Materials	15	25-Mar-21	14-Apr-21						█								
Floorcovering - Place Material Orders	30	25-Mar-21	05-May-21						█								
Design Review & Approve Fire Protection Submittal	10	01-Apr-21	14-Apr-21						█								
Design Review & Approve Structural Steel Submitt	10	01-Apr-21	14-Apr-21						█								
Design Review & Approve Interior Glass & Glazing :	10	01-Apr-21	14-Apr-21						█								
Design Review & Approve Millwork Submittals	10	01-Apr-21	14-Apr-21						█								
Mechanical - Release & Fabricate Equipment	30	01-Apr-21	12-May-21						█								
Electrical - Release & Fabricate Equipment	30	01-Apr-21	12-May-21						█								
Doors, Frames & Hardware - Release & Fabricate t	20	01-Apr-21	28-Apr-21						█								
Doors, Frames & Hardware - Release & Fabricate \	60	01-Apr-21	23-Jun-21						█								
Doors, Frames & Hardware - Release & Procure D	60	01-Apr-21	23-Jun-21						█								

Activity Name	Original Duration	Start	Finish	2020		2021											
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep			
GC Review & Submit Kitchen Equipment Submittal	5	02-Apr-21	08-Apr-21								■						
Design Review & Approve Kitchen Equipment Subr	10	06-Apr-21	19-Apr-21								■						
Fire Protection - Release & Procure Materials	15	15-Apr-21	05-May-21								■						
Structural Steel - Fabricate & Deliver Steel	30	15-Apr-21	26-May-21								■						
Interior Glass & Glazing - Release & Procure Framir	40	15-Apr-21	09-Jun-21								■						
Millwork - Release Material Orders & Fabricate	50	15-Apr-21	23-Jun-21								■						
Kitchen Equipment - Release & Procure Equipmen	40	20-Apr-21	14-Jun-21								■						
<b>Permitting</b>	<b>48</b>	<b>05-Feb-21</b>	<b>13-Apr-21</b>														
Workplace Permitting	15	05-Feb-21	25-Feb-21														
Test Kitchen Permitting	15	24-Mar-21	13-Apr-21														
<b>Interior Build-out</b>	<b>89</b>	<b>26-Feb-21</b>	<b>30-Jun-21</b>														
<b>Monumental Stair</b>	<b>81</b>	<b>26-Feb-21</b>	<b>18-Jun-21</b>														
Field Dimensioning	8	26-Feb-21	09-Mar-21								■						
Temp. Structure Shoring	5	10-Mar-21	16-Mar-21								■						
Structural Demolition for Staircase (Slab Opening)	6	17-Mar-21	24-Mar-21								■						
Staircase / Existing Building Connections Install	10	25-Mar-21	07-Apr-21								■						
Install Temp Walls in Stair Area	3	25-Mar-21	29-Mar-21								■						
Install Stair Structural Components	10	08-Apr-21	21-Apr-21								■						
Stair Treads & Risers Construction	12	22-Apr-21	07-May-21								■						
Stair Finish Materials Installed (Soffits / Tread Finish	10	10-May-21	21-May-21								■						
Glass / Metal Railings	12	24-May-21	08-Jun-21								■						
Handrails	8	09-Jun-21	18-Jun-21								■						
<b>Lower Floor</b>	<b>81</b>	<b>26-Feb-21</b>	<b>18-Jun-21</b>														
<b>Office Spaces</b>	<b>65</b>	<b>26-Feb-21</b>	<b>27-May-21</b>														
MEP OH Rough-in	8	26-Feb-21	09-Mar-21								■						
Metal Stud Partition / Furring	7	10-Mar-21	18-Mar-21								■						
Frame Hard Ceilings & Soffits	3	19-Mar-21	23-Mar-21								■						
AV / Low-Voltage Wiring Rough-in	4	19-Mar-21	24-Mar-21								■						
MEP Wall Rough-in	8	19-Mar-21	30-Mar-21								■						
MEP Rough-in Hard Ceilings & Soffits	4	24-Mar-21	29-Mar-21								■						
Hang Hard Ceilings & Soffits	3	30-Mar-21	01-Apr-21								■						
Drywall Hang & Finish	8	31-Mar-21	09-Apr-21								■						
Finish Hard Ceilings & Soffits	4	02-Apr-21	07-Apr-21								■						
Floor & Wall Tile	4	08-Apr-21	13-Apr-21								■						
ACT Grid	6	12-Apr-21	19-Apr-21								■						
MEP Acoustical Ceiling Rough-in	6	20-Apr-21	27-Apr-21								■						
Above Ceiling Inspections	2	28-Apr-21	29-Apr-21								■						

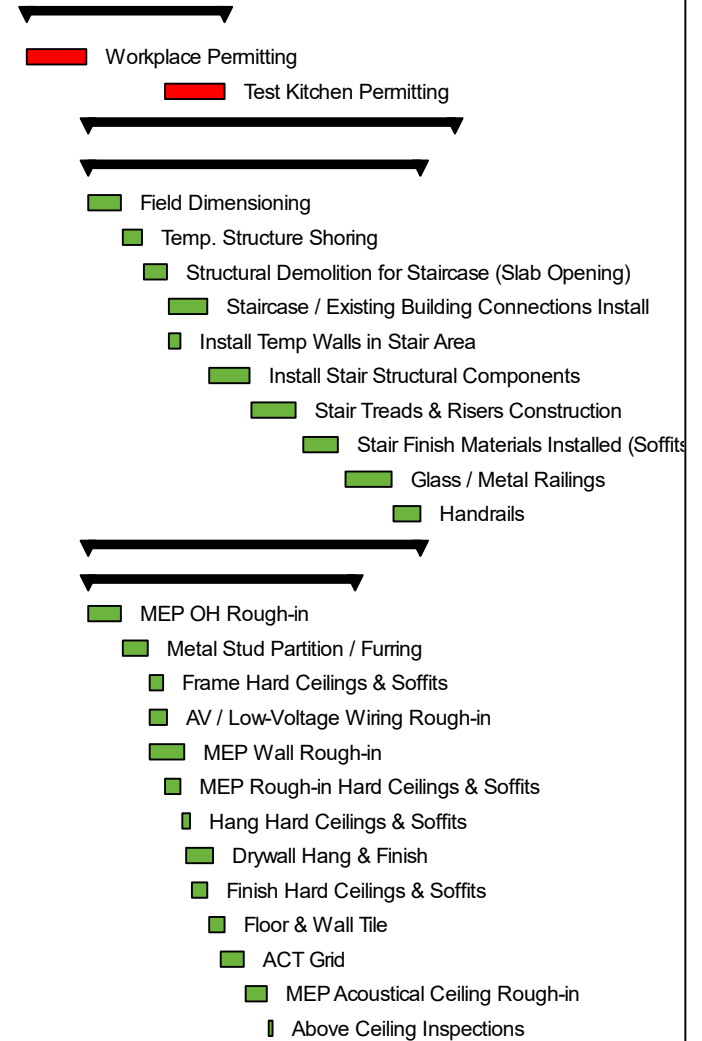

Activity Name	Original Duration	Start	Finish	2020			2021					
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
Drop Ceiling Tile	3	30-Apr-21	04-May-21								■	Drop Ceiling Tile
Soft Flooring Install	4	05-May-21	10-May-21								■	Soft Flooring Install
Casework / Millwork Install	5	11-May-21	17-May-21								■	Casework / Millwork Install
Wood Door Install	4	18-May-21	21-May-21								■	Wood Door Install
MEP Trim-out & Fixtures	6	18-May-21	25-May-21								■	MEP Trim-out & Fixtures
Finish Paint	5	18-May-21	24-May-21								■	Finish Paint
Door Hardware Install	4	24-May-21	27-May-21								■	Door Hardware Install
Specialties Install	2	25-May-21	26-May-21								■	Specialties Install
Signage Install	3	25-May-21	27-May-21								■	Signage Install
<b>Collaboration Spaces / War Rooms</b>	<b>63</b>	<b>10-Mar-21</b>	<b>04-Jun-21</b>									
MEP OH Rough-in	8	10-Mar-21	19-Mar-21								■	MEP OH Rough-in
Metal Stud Partition / Furring	7	22-Mar-21	30-Mar-21								■	Metal Stud Partition / Furring
Frame Hard Ceilings & Soffits	3	31-Mar-21	02-Apr-21								■	Frame Hard Ceilings & Soffits
AV / Low-Voltage Wiring Rough-in	4	31-Mar-21	05-Apr-21								■	AV / Low-Voltage Wiring Rough-in
MEP Wall Rough-in	4	31-Mar-21	05-Apr-21								■	MEP Wall Rough-in
MEP Rough-in Hard Ceilings & Soffits	4	05-Apr-21	08-Apr-21								■	MEP Rough-in Hard Ceilings & Soffits
Drywall Hang & Finish	6	06-Apr-21	13-Apr-21								■	Drywall Hang & Finish
Hang Hard Ceilings & Soffits	3	09-Apr-21	13-Apr-21								■	Hang Hard Ceilings & Soffits
Finish Hard Ceilings & Soffits	4	14-Apr-21	19-Apr-21								■	Finish Hard Ceilings & Soffits
ACT Grid	6	20-Apr-21	27-Apr-21								■	ACT Grid
Floor & Wall Tile	4	20-Apr-21	23-Apr-21								■	Floor & Wall Tile
MEP Acoustical Ceiling Rough-in	6	28-Apr-21	05-May-21								■	MEP Acoustical Ceiling Rough-in
Above Ceiling Inspections	2	06-May-21	07-May-21								■	Above Ceiling Inspections
Drop Ceiling Tile	3	10-May-21	12-May-21								■	Drop Ceiling Tile
Soft Flooring Install	4	13-May-21	18-May-21								■	Soft Flooring Install
Casework / Millwork Install	5	19-May-21	25-May-21								■	Casework / Millwork Install
Wood Door Install	4	26-May-21	31-May-21								■	Wood Door Install
MEP Trim-out & Fixtures	6	26-May-21	02-Jun-21								■	MEP Trim-out & Fixtures
Finish Paint	5	26-May-21	01-Jun-21								■	Finish Paint
Door Hardware Install	4	01-Jun-21	04-Jun-21								■	Door Hardware Install
Specialties Install	2	02-Jun-21	03-Jun-21								■	Specialties Install
Signage Install	3	02-Jun-21	04-Jun-21								■	Signage Install
<b>Employee Gym / Locker Rooms / Showers</b>	<b>65</b>	<b>22-Mar-21</b>	<b>18-Jun-21</b>									
MEP OH Rough-in	8	22-Mar-21	31-Mar-21								■	MEP OH Rough-in
Metal Stud Partition / Furring	7	01-Apr-21	09-Apr-21								■	Metal Stud Partition / Furring
Frame Hard Ceilings & Soffits	3	12-Apr-21	14-Apr-21								■	Frame Hard Ceilings & Soffits
MEP Wall Rough-in	6	12-Apr-21	19-Apr-21								■	MEP Wall Rough-in
MEP Rough-in Hard Ceilings & Soffits	4	15-Apr-21	20-Apr-21								■	MEP Rough-in Hard Ceilings & Soffits



Activity Name	Original Duration	Start	Finish	2020		2021								
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
Drywall Hang & Finish	5	20-Apr-21	26-Apr-21								■	Drywall Hang & Finish		
Hang Hard Ceilings & Soffits	3	21-Apr-21	23-Apr-21								■	Hang Hard Ceilings & Soffits		
Finish Hard Ceilings & Soffits	4	26-Apr-21	29-Apr-21								■	Finish Hard Ceilings & Soffits		
ACT Grid	6	30-Apr-21	07-May-21								■	ACT Grid		
Floor & Wall Tile	4	30-Apr-21	05-May-21								■	Floor & Wall Tile		
Locker Install	5	06-May-21	12-May-21								■	Locker Install		
MEP Acoustical Ceiling Rough-in	6	10-May-21	17-May-21								■	MEP Acoustical Ceiling Rough-in		
Above Ceiling Inspections	2	18-May-21	19-May-21								■	Above Ceiling Inspections		
Drop Ceiling Tile	3	20-May-21	24-May-21								■	Drop Ceiling Tile		
Soft Flooring Install	4	25-May-21	28-May-21								■	Soft Flooring Install		
Casework / Millwork Install	5	31-May-21	04-Jun-21								■	Casework / Millwork Install		
Wood Door Install	4	07-Jun-21	10-Jun-21								■	Wood Door Install		
MEP Trim-out & Fixtures	6	07-Jun-21	14-Jun-21								■	MEP Trim-out & Fixtures		
Finish Paint	5	07-Jun-21	11-Jun-21								■	Finish Paint		
Door Hardware Install	4	11-Jun-21	16-Jun-21								■	Door Hardware Install		
Specialties Install	2	14-Jun-21	15-Jun-21								■	Specialties Install		
Signage Install	3	14-Jun-21	16-Jun-21								■	Signage Install		
Shower / Locker Room Benches	5	14-Jun-21	18-Jun-21								■	Shower / Locker Room Benches		
Toilet Partitions / Accessories Install	5	14-Jun-21	18-Jun-21								■	Toilet Partitions / Accessories Install		
<b>Training Room</b>	<b>56</b>	<b>01-Apr-21</b>	<b>17-Jun-21</b>											
MEP OH Rough-in	8	01-Apr-21	12-Apr-21								■	MEP OH Rough-in		
Metal Stud Partition / Furring	7	13-Apr-21	21-Apr-21								■	Metal Stud Partition / Furring		
AV / Low-Voltage Wiring Rough-in	4	22-Apr-21	27-Apr-21								■	AV / Low-Voltage Wiring Rough-in		
MEP Wall Rough-in	2	22-Apr-21	23-Apr-21								■	MEP Wall Rough-in		
Drywall Hang & Finish	3	28-Apr-21	30-Apr-21								■	Drywall Hang & Finish		
ACT Grid	6	03-May-21	10-May-21								■	ACT Grid		
MEP Acoustical Ceiling Rough-in	6	11-May-21	18-May-21								■	MEP Acoustical Ceiling Rough-in		
Above Ceiling Inspections	2	19-May-21	20-May-21								■	Above Ceiling Inspections		
Drop Ceiling Tile	3	21-May-21	25-May-21								■	Drop Ceiling Tile		
Soft Flooring Install	4	26-May-21	31-May-21								■	Soft Flooring Install		
Casework / Millwork Install	5	01-Jun-21	07-Jun-21								■	Casework / Millwork Install		
Wood Door Install	4	08-Jun-21	11-Jun-21								■	Wood Door Install		
MEP Trim-out	6	08-Jun-21	15-Jun-21								■	MEP Trim-out		
Finish Paint	5	08-Jun-21	14-Jun-21								■	Finish Paint		
Door Hardware Install	4	14-Jun-21	17-Jun-21								■	Door Hardware Install		
Specialties Install	2	15-Jun-21	16-Jun-21								■	Specialties Install		
<b>Upper Floor</b>	<b>89</b>	<b>26-Feb-21</b>	<b>30-Jun-21</b>											
<b>Reception</b>	<b>63</b>	<b>26-Feb-21</b>	<b>25-May-21</b>											



Activity Name	Original Duration	Start	Finish	2020				2021						
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
MEP OH Rough-in	8	26-Feb-21	09-Mar-21					■						
Metal Stud Partition / Furring	7	10-Mar-21	18-Mar-21					■						
Frame Hard Ceilings & Soffits	3	19-Mar-21	23-Mar-21					■						
AV / Low-Voltage Wiring Rough-in	4	19-Mar-21	24-Mar-21					■						
MEP Wall Rough-in	2	19-Mar-21	22-Mar-21					■						
MEP Rough-in Hard Ceilings & Soffits	4	24-Mar-21	29-Mar-21					■						
Drywall Hang & Finish	4	25-Mar-21	30-Mar-21					■						
Hang Hard Ceilings & Soffits	3	30-Mar-21	01-Apr-21					■						
Finish Hard Ceilings & Soffits	4	02-Apr-21	07-Apr-21					■						
ACT Grid	6	08-Apr-21	15-Apr-21					■						
Floor & Wall Tile	4	08-Apr-21	13-Apr-21					■						
MEP Acoustical Ceiling Rough-in	6	16-Apr-21	23-Apr-21					■						
Above Ceiling Inspections	2	26-Apr-21	27-Apr-21					■						
Drop Ceiling Tile	3	28-Apr-21	30-Apr-21					■						
Soft Flooring Install	4	03-May-21	06-May-21					■						
Casework / Millwork Install	5	07-May-21	13-May-21					■						
Wood Door Install	4	14-May-21	19-May-21					■						
MEP Trim-out & Fixtures	6	14-May-21	21-May-21					■						
Finish Paint	5	14-May-21	20-May-21					■						
Door Hardware Install	4	20-May-21	25-May-21					■						
Specialties Install	2	21-May-21	24-May-21					■						
Signage Install	3	21-May-21	25-May-21					■						
<b>Collaboration Spaces</b>	<b>63</b>	<b>10-Mar-21</b>	<b>04-Jun-21</b>											
MEP OH Rough-in	8	10-Mar-21	19-Mar-21					■						
Metal Stud Partition / Furring	7	22-Mar-21	30-Mar-21					■						
Frame Hard Ceilings & Soffits	3	31-Mar-21	02-Apr-21					■						
AV / Low-Voltage Wiring Rough-in	4	31-Mar-21	05-Apr-21					■						
MEP Wall Rough-in	3	31-Mar-21	02-Apr-21					■						
MEP Rough-in Hard Ceilings & Soffits	4	05-Apr-21	08-Apr-21					■						
Drywall Hang & Finish	6	06-Apr-21	13-Apr-21					■						
Hang Hard Ceilings & Soffits	3	09-Apr-21	13-Apr-21					■						
Finish Hard Ceilings & Soffits	4	14-Apr-21	19-Apr-21					■						
ACT Grid	6	20-Apr-21	27-Apr-21					■						
Floor & Wall Tile	4	20-Apr-21	23-Apr-21					■						
MEP Acoustical Ceiling Rough-in	6	28-Apr-21	05-May-21					■						
Above Ceiling Inspections	2	06-May-21	07-May-21					■						
Drop Ceiling Tile	3	10-May-21	12-May-21					■						
Soft Flooring Install	4	13-May-21	18-May-21					■						

- MEP OH Rough-in
- Metal Stud Partition / Furring
- Frame Hard Ceilings & Soffits
- AV / Low-Voltage Wiring Rough-in
- MEP Wall Rough-in
- MEP Rough-in Hard Ceilings & Soffits
- Drywall Hang & Finish
- Hang Hard Ceilings & Soffits
- Finish Hard Ceilings & Soffits
- ACT Grid
- Floor & Wall Tile
- MEP Acoustical Ceiling Rough-in
- Above Ceiling Inspections
- Drop Ceiling Tile
- Soft Flooring Install



Activity Name	Original Duration	Start	Finish	2020				2021				
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
Casework / Millwork Install	5	19-May-21	25-May-21								■	Casework / Millwork Install
Wood Door Install	4	26-May-21	31-May-21								■	Wood Door Install
MEP Trim-out & Fixtures	6	26-May-21	02-Jun-21								■	MEP Trim-out & Fixtures
Finish Paint	5	26-May-21	01-Jun-21								■	Finish Paint
Door Hardware Install	4	01-Jun-21	04-Jun-21								■	Door Hardware Install
Specialties Install	2	02-Jun-21	03-Jun-21								■	Specialties Install
Signage Install	3	02-Jun-21	04-Jun-21								■	Signage Install
<b>ELT Offices</b>	<b>63</b>	<b>22-Mar-21</b>	<b>16-Jun-21</b>									
MEP OH Rough-in	8	22-Mar-21	31-Mar-21								■	MEP OH Rough-in
Metal Stud Partition / Furring	7	01-Apr-21	09-Apr-21								■	Metal Stud Partition / Furring
Frame Hard Ceilings & Soffits	3	12-Apr-21	14-Apr-21								■	Frame Hard Ceilings & Soffits
AV / Low-Voltage Wiring Rough-in	4	12-Apr-21	15-Apr-21								■	AV / Low-Voltage Wiring Rough-in
MEP Wall Rough-in	4	12-Apr-21	15-Apr-21								■	MEP Wall Rough-in
MEP Rough-in Hard Ceilings & Soffits	4	15-Apr-21	20-Apr-21								■	MEP Rough-in Hard Ceilings & Soffits
Drywall Hang & Finish	5	16-Apr-21	22-Apr-21								■	Drywall Hang & Finish
Hang Hard Ceilings & Soffits	3	21-Apr-21	23-Apr-21								■	Hang Hard Ceilings & Soffits
Finish Hard Ceilings & Soffits	4	26-Apr-21	29-Apr-21								■	Finish Hard Ceilings & Soffits
ACT Grid	6	30-Apr-21	07-May-21								■	ACT Grid
Floor & Wall Tile	4	30-Apr-21	05-May-21								■	Floor & Wall Tile
MEP Acoustical Ceiling Rough-in	6	10-May-21	17-May-21								■	MEP Acoustical Ceiling Rough-in
Above Ceiling Inspections	2	18-May-21	19-May-21								■	Above Ceiling Inspections
Drop Ceiling Tile	3	20-May-21	24-May-21								■	Drop Ceiling Tile
Soft Flooring Install	4	25-May-21	28-May-21								■	Soft Flooring Install
Casework / Millwork Install	5	31-May-21	04-Jun-21								■	Casework / Millwork Install
Wood Door Install	4	07-Jun-21	10-Jun-21								■	Wood Door Install
MEP Trim-out & Fixtures	6	07-Jun-21	14-Jun-21								■	MEP Trim-out & Fixtures
Finish Paint	5	07-Jun-21	11-Jun-21								■	Finish Paint
Door Hardware Install	4	11-Jun-21	16-Jun-21								■	Door Hardware Install
Specialties Install	2	14-Jun-21	15-Jun-21								■	Specialties Install
Signage Install	3	14-Jun-21	16-Jun-21								■	Signage Install
<b>Hospitality Area</b>	<b>65</b>	<b>01-Apr-21</b>	<b>30-Jun-21</b>									
MEP OH Rough-in	8	01-Apr-21	12-Apr-21								■	MEP OH Rough-in
Metal Stud Partition / Furring	7	13-Apr-21	21-Apr-21								■	Metal Stud Partition / Furring
Frame Hard Ceilings & Soffits	3	22-Apr-21	26-Apr-21								■	Frame Hard Ceilings & Soffits
AV / Low-Voltage Wiring Rough-in	4	22-Apr-21	27-Apr-21								■	AV / Low-Voltage Wiring Rough-in
MEP Wall Rough-in	4	22-Apr-21	27-Apr-21								■	MEP Wall Rough-in
MEP Rough-in Hard Ceilings & Soffits	4	27-Apr-21	30-Apr-21								■	MEP Rough-in Hard Ceilings & Soffits
Drywall Hang & Finish	3	28-Apr-21	30-Apr-21								■	Drywall Hang & Finish



Activity Name	Original Duration	Start	Finish	2020				2021					
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
Hang Hard Ceilings & Soffits	3	03-May-21	05-May-21									■	Hang Hard Ceilings & Soffits
Finish Hard Ceilings & Soffits	4	06-May-21	11-May-21									■	Finish Hard Ceilings & Soffits
ACT Grid	6	12-May-21	19-May-21									■	ACT Grid
Floor & Wall Tile	4	12-May-21	17-May-21									■	Floor & Wall Tile
MEP Acoustical Ceiling Rough-in	6	20-May-21	27-May-21									■	MEP Acoustical Ceiling Rough-in
Above Ceiling Inspections	2	28-May-21	31-May-21									■	Above Ceiling Inspections
Drop Ceiling Tile	3	01-Jun-21	03-Jun-21									■	Drop Ceiling Tile
Soft Flooring Install	4	04-Jun-21	09-Jun-21									■	Soft Flooring Install
Casework / Millwork Install	5	10-Jun-21	16-Jun-21									■	Casework / Millwork Install
MEP Trim-out	6	17-Jun-21	24-Jun-21									■	MEP Trim-out
Finish Paint	5	17-Jun-21	23-Jun-21									■	Finish Paint
Specialties Install	2	24-Jun-21	25-Jun-21									■	Specialties Install
Signage Install	3	24-Jun-21	28-Jun-21									■	Signage Install
Install Bar Equipment	5	24-Jun-21	30-Jun-21									■	Install Bar Equipment
<b>Test Kitchen</b>	<b>53</b>	<b>14-Apr-21</b>	<b>25-Jun-21</b>										
MEP OH Rough-in	8	14-Apr-21	23-Apr-21									■	MEP OH Rough-in
Metal Stud Partition / Furring	7	26-Apr-21	04-May-21									■	Metal Stud Partition / Furring
Frame Hard Ceilings & Soffits	3	05-May-21	07-May-21									■	Frame Hard Ceilings & Soffits
AV / Low-Voltage Wiring Rough-in	4	05-May-21	10-May-21									■	AV / Low-Voltage Wiring Rough-in
MEP Wall Rough-in	6	05-May-21	12-May-21									■	MEP Wall Rough-in
MEP Rough-in Hard Ceilings & Soffits	4	10-May-21	13-May-21									■	MEP Rough-in Hard Ceilings & Soffits
Drywall Hang & Finish	4	13-May-21	18-May-21									■	Drywall Hang & Finish
Hang Hard Ceilings & Soffits	3	14-May-21	18-May-21									■	Hang Hard Ceilings & Soffits
Finish Hard Ceilings & Soffits	4	19-May-21	24-May-21									■	Finish Hard Ceilings & Soffits
ACT Grid	6	25-May-21	01-Jun-21									■	ACT Grid
Floor & Wall Tile	4	25-May-21	28-May-21									■	Floor & Wall Tile
Casework / Millwork Install	5	31-May-21	04-Jun-21									■	Casework / Millwork Install
MEP Acoustical Ceiling Rough-in	6	02-Jun-21	09-Jun-21									■	MEP Acoustical Ceiling Rough-in
MEP Trim-out	6	07-Jun-21	14-Jun-21									■	MEP Trim-out
Finish Paint	5	07-Jun-21	11-Jun-21									■	Finish Paint
Install Kitchen Equipment & Final Connections	15	07-Jun-21	25-Jun-21									■	Install Kitchen Equipment
Above Ceiling Inspections	2	10-Jun-21	11-Jun-21									■	Above Ceiling Inspections
Drop Ceiling Tile	3	14-Jun-21	16-Jun-21									■	Drop Ceiling Tile
Specialties Install	2	14-Jun-21	15-Jun-21									■	Specialties Install
Signage Install	3	14-Jun-21	16-Jun-21									■	Signage Install
<b>Inspections</b>	<b>5</b>	<b>25-Jun-21</b>	<b>01-Jul-21</b>										
Final Plumbing Inspection	2	25-Jun-21	28-Jun-21									■	Final Plumbing Inspection



Activity Name	Original Duration	Start	Finish	2020		2021														
				Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep						
Final Mechanical Inspection	2	25-Jun-21	28-Jun-21																	■ Final Mechanical Inspect
Final Electrical Inspection	3	25-Jun-21	29-Jun-21																	■ Final Electrical Inspectio
Final Fire Inspection	1	25-Jun-21	25-Jun-21																	■ Final Fire Inspection
Final Health Department Inspection	2	28-Jun-21	29-Jun-21																	■ Final Health Departmen
Final Building Inspection	2	30-Jun-21	01-Jul-21																	■ Final Building Inspectio
<b>Close-out</b>	<b>73</b>	<b>23-Mar-21</b>	<b>01-Jul-21</b>																	
Contractor Prepare & Submit Initial Closeout Docume	20	23-Mar-21	19-Apr-21																	■ Contractor Prepare & Submit Initial Closeout D
Design Team Review Initial Closeout Documents	20	20-Apr-21	17-May-21																	■ Design Team Review Initial Closeout I
Finalize & Submit Closeout Documents and As-Builts	20	18-May-21	14-Jun-21																	■ Finalize & Submit Closeout D
Owner / Design Team Punchlist (Create & Distribute)	5	28-May-21	03-Jun-21																	■ Owner / Design Team Punchlist
Owner / Design Team Punchlist (Complete & Check-of	20	04-Jun-21	01-Jul-21																	■ Owner / Design Team P
